

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 057
Date: 2014-11-06
Day: Thursday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: cloudy
Temperature: 7:30 am: 40°

Noon: rain
Noon: 48°

3:00 pm: rain
3:00 pm: 48°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	0	3	4
	Div. 04		Masonry	1	0	3	4
	09 90 00		Painting	0	0	0	0
	02 41 19		Demolition	1	0	3	4
Subcontractors:	02 08 00	A & J Demo Services	Asbestos Abatement	1	0	3	4
	26 00 00	Griffin Electric	Electrician	1	0	0	1
	22 00 00	Lapan Mechanical	Plumber	0	0	0	0
	03 30 00	Precision Concrete	CIP Concrete	0	0	0	0
	07 31 00	Meadows Construction	Synthetic Slate Shingles	1	0	4	5
Total:				6	0	15	21

DAILY REPORT

Activities Today:

- 1) Masons: removing individual brick on the south elevation of the south wing; pointing on the west elevation (*this work was suspended for the day due to rain*)
- 2) Roofers: continuing with the shingle installation on the east elevation of the main building (*this work was suspended for the day due to rain*)
- 3) Carpenters: laying out LVLs for framing in the meeting hall; installing existing posts on new footings in the basement
- 4) Demo: removing debris from building; general site cleaning; assisting with post installation
- 5) Abatement: starting roof abatement on the north elevation of the meeting hall (*this work was suspended for the day due to rain*)
- 6) Electrician: was on site in the afternoon to start removing electrical equipment from the basement now that the transformer has been removed

Copies to: Richard Montuori, Town of Tewksbury
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI
Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects

PHOTO INDEX



Photo showing roofers working on the east elevation of the main building before the rain started.



Photo showing the roofers installing the new shingles.



Photo showing the abatement crew working on the north side of the meeting hall roof before the rain started.



Photo showing abatement crew cleaning up before stopping for the day.



Photo showing the rim joists installed around the meeting hall perimeter.

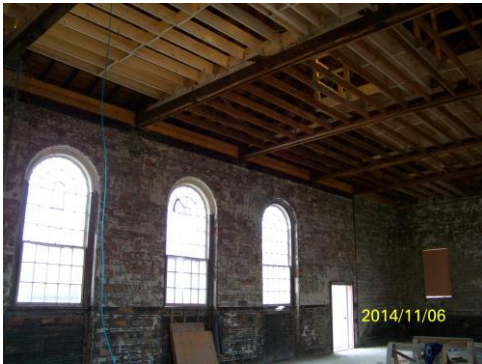


Photo showing additional rim joists around the meeting hall.



Photo showing the existing posts being installed.



Photo showing an existing post back in place.



Photo showing laborer collecting debris for disposal.



Photo showing electrician working on removing the equipment now that the transformer has been removed.



Photo showing some of the new steel on site.
