

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
 Report No. 159
 Date: 2015-04-08
 Day: Wednesday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: clear

Temperature: 7:30 am: 31°

Noon: cloudy

Noon: 39°

3:00 pm: light flurries

3:00 pm: 36°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	6	1	6
	Div. 04		Masonry	1	0	1	2
	09 90 00		Paint/Plaster	0	0	0	0
	02 41 19		Labor	1	2	0	3
	Div. 31		Site Work	0	0	0	0
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	1	0	0	1
	07 21 00		Insulation	0	0	0	0
Subcontractors:	02 08 00	A & J Demo Services	Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	07 31 00	Meadows Construction	Roofing	1	1	0	2
	07 53 00						
	07 61 19	Ambient Temp. Corp.	HVAC	2	5	1	8
	Div. 23						
Total:	Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0
				8	15	3	26

DAILY REPORT

Activities Today:

- 1) **Carpentry:** continuing to install GWB in the basement; blocking in the chase on the 2nd floor; installing GWB in the stairwells; installing blocking in the ceiling framing in the meeting hall;
- 2) **Electrical:** continuing with in-wall rough installation on all floors
- 3) **HVAC:** continuing with mechanical piping and equipment installation on all floors; continuing with insulation of piping on all floors; testing parts of the system
- 4) **Labor:** general site cleaning; assisting other trades; cutting out window in basement to make new doorway; getting ready to receive vault delivery scheduled for tomorrow
- 5) **Concrete:** installing reinforcement for slabs
- 6) **Masonry:** blocked in opening in masonry wall in the basement; infilling voids in walls in stairwell #2; installing stone sill on basement window on the west elevation
- 7) **Roofing:** installing the copper flashing and PVC trim along the base of the cupola; installing copper ridge cap on main roof; working on flashing on the southwest end of the meeting hall roof

PHOTO INDEX



Photo showing some of the duct insulation that has been installed.



Photo showing some of the attic insulation that has been installed.



Photo showing blocked-in opening getting the room ready for the vault.



Photo showing duct insulation being installed in the basement.



Photo showing GWB being installed in stair #2 stairwell.



Photo showing GWB being installed in stair #3 stairwell.

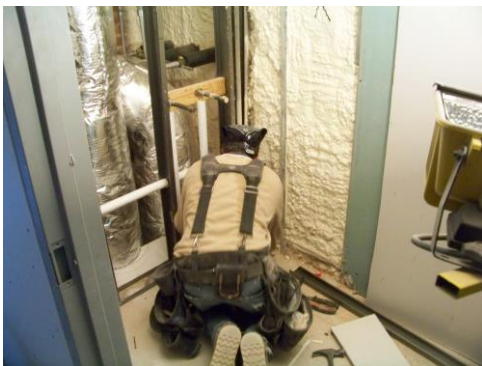


Photo showing carpenter blocking in a chase on the 2nd floor.

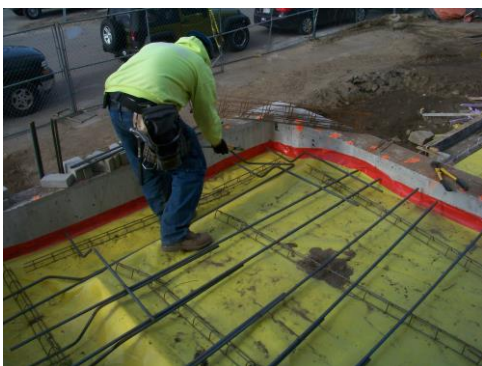


Photo showing workman installing reinforcement for the vault slab in the addition.



Photo showing roofer installing bottom trim at the base of the cupola.



Photo showing workmen demolishing a window opening to make a doorway.



Photo showing some of the HVAC piping in the attic.



Photo showing pipe chase on the 2nd floor.

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
