

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 185
Date: 2015-05-15
Day: Friday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: clear

Temperature: 7:30 am: 50°

Noon: overcast

Noon: 68°

3:00 pm: overcast

3:00 pm: 69°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	3	0	4
	Div. 04		Masonry	1	1	2	4
	09 90 00		Paint/Plaster	1	1	0	2
	02 41 19		Labor	1	0	0	1
	Div. 31		Site Work	0	0	0	0
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
	07 21 00		Insulation	0	0	0	0
Subcontractors:	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	07 31 00	Meadows Construction	Roofing	0	0	0	0
	07 53 00						
	07 61 19	Ambient Temp. Corp.	HVAC	1	0	0	1
	Div. 23						
	Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0
Total:	13 27 16	Fire Lock	Modular Fire Vault	0	0	0	0
				6	6	2	14

DAILY REPORT

Activities Today:

- 1) Carpentry: finishing sheetrock installation on the ceiling of the meeting hall; installing furring channels for stairway #2; starting to frame the soffit for stairway #2; starting to frame the stairs for the platform
- 2) HVAC: installing fin tube radiation in the basement
- 3) Labor: one laborer is working with the masons; one laborer is performing general site cleaning
- 4) Masonry: continuing with the installation of CMU blocks for the addition
- 5) Paint/Plaster: continuing with taping & mudding joints on the 1st floor; priming and painting on the 1st floor
- 6) Electrical: installing 4" sleeves for telephone lines
- 7) Misc.: water main line was flushed today and chlorine added. The Town will test the water on Monday.

PHOTO INDEX





	<p>Photo showing carpenter working on installing the furring channels on the underside of the stairs.</p>
	<p>Photo showing the furring channels installed on the underside of the stairs.</p>
	<p>Photo showing soffit framing taking shape at the bottom of stair #2.</p>
	<p>Photo showing workman applying joint compound to the sheetrock in meeting room 114.</p>



Photo showing the walls in meeting room 114 being primed.



Photo showing cores made by the electrician for the telephone and data service.



Photo showing carpenters locating soffit lights in meeting hall.

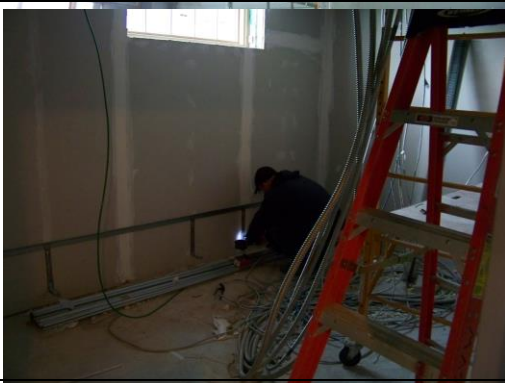




Photo showing HVAC tech installing fin tube radiation.

	<p>Photo showing some of the fin tube radiation in place in the basement.</p>
	<p>Photo showing masons continuing to lay CMU block for the addition.</p>

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
