




## TEWKSBURY WTF IMPROVEMENTS PROJECT

Weekly Progress Report for Week Ending: February 26, 2016

Design Engineer: AECOM  
General Contractor: Kinsmen Corporation

### I. Work Performed Last Week:

- A manufacturer's representative from Aqua Aerobics was onsite for inspection of the filter rehabilitation work.
- The contractor completed the installation of the porous plates and the lower level cell divider adjustment rods.
- The contractor completed the upper cell divider wall angles.
- Several shipments deliveries were made to the site including the delivery of filter replacement parts and electrical materials.
- The electrician worked on the new conduits in the generator. The electrician continued setting up their field trailer.

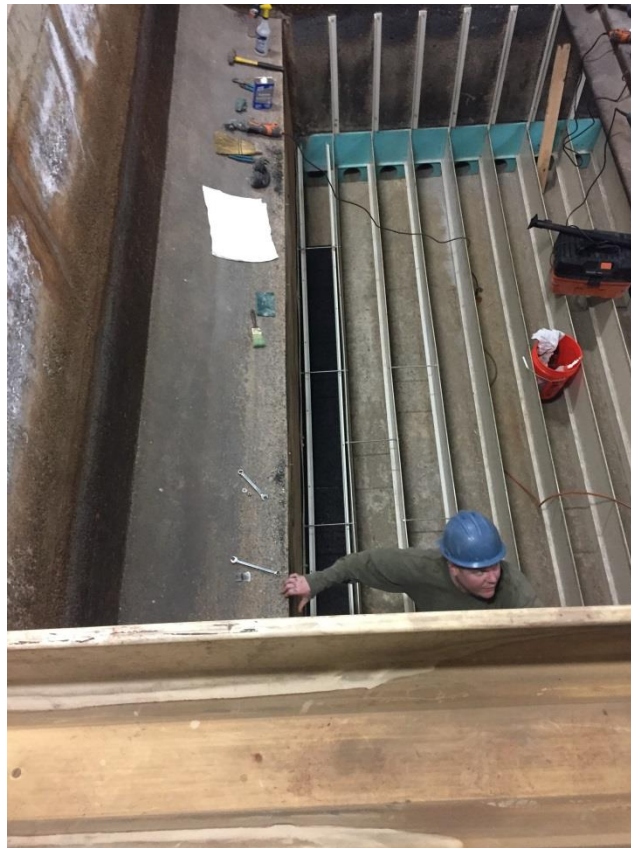

*Start of the porous plate installation between lower cell dividers.*



*Partial completion of porous plates & adjustment rods.*



*Final completion of porous plates & cell divider adjustment rods.*

## **II. Construction / Public Relation Issues:**

- The contractor was reminded to maintain a safe work environment.

## **III. Erosion and Sedimentation Control:**

- The contractor maintained the silt sock placed at the bottom of the front slope.
- Erosion control will be monitored and maintained throughout the project.

## **IV. Upcoming Work for Next Week:**

- Filter No. 1 - Electrical work.
- Filter No. 1 – Continue with the installation of the new FRP components.
- Expected delivery of the remaining filter replacement parts.

## **V. Notes:**

- The next progress meeting is scheduled for Thursday, March 3, 2016.

Ted Angelakis  
**AECOM Resident Representative**
