



TEWKSBURY WTF IMPROVEMENTS PROJECT

Weekly Progress Report for Week Ending: March 11, 2016

Design Engineer: AECOM
General Contractor: Kinsmen Corporation

I. Work Performed Last Week:

- The crews installed approximately 11" of new sand media in Filter No. 1. The WTF staff backwashed the sand after the installation.
- The crews installed approximately 36" of regenerated activated carbon media in Filter No. 1. The WTF staff backwashed the carbon after the installation. However, the filter was not put back into service while awaiting a representative from Aqua Aerobics to conduct a final checkout.
- The crews prepped the materials necessary for the Filter No. 2 work; moving the filter replacement parts into the building.
- The electricians started installation of the fire alarm conduits in Filter Room No. 3 & 4. The electricians worked in this area all week.




Installation of new sand media for Filter No. 1.



Installation of regenerated activated carbon for Filter No. 1.



Sliding cover installed by Electricians over Filter Nos. 3 & 4.

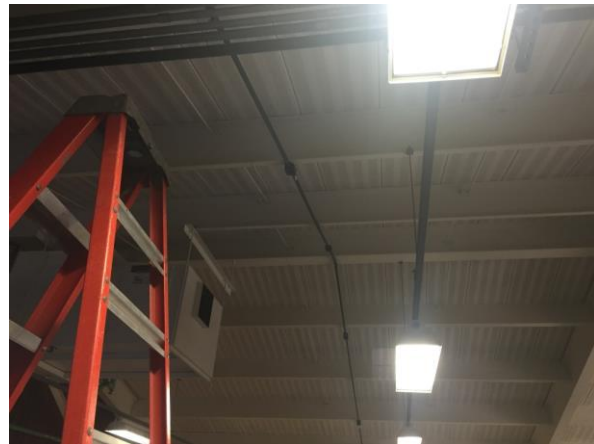

New fire alarm conduit installed by Electricians in Filter Room.

II. Construction / Public Relation Issues:

- The contractor was reminded to maintain a safe work environment.

III. Erosion and Sedimentation Control:

- The contractor maintained the silt sock placed at the bottom of the front slope.
- Erosion control will be monitored and maintained throughout the project.

IV. Upcoming Work for Next Week:

- Filter No. 1 – Manufacturer's checkout.
- Filter No. 1 – Re-activation into service.
- Filter No. 2 – Carbon and sand removal.

V. Notes:

- The next progress meeting is scheduled for Thursday, April 7, 2016.

Ted Angelakis
AECOM Resident Representative
