



TEWKSBURY WTF IMPROVEMENTS PROJECT

Weekly Progress Report for Week Ending: April 8, 2016


Design Engineer: AECOM
General Contractor: Kinsmen Corporation

I. Work Performed Last Week:

- The crews completed the coating of the Filter No. 2 effluent channel.
- The crews performed the final cleanup of the porous cell plates.
- The crews worked on the site layout for the new sludge storage tank.
- The crews painted the bridge track rails.
- The crews cleaned up around the filter room areas.
- The electricians continued with the installation of the fire alarm conduit components on the walls and ceilings in Filter Room No. 1 and 2.
- A monthly progress meeting was held at the WTF.



Painted track rail for Filter No. 2 travelling bridge assembly.

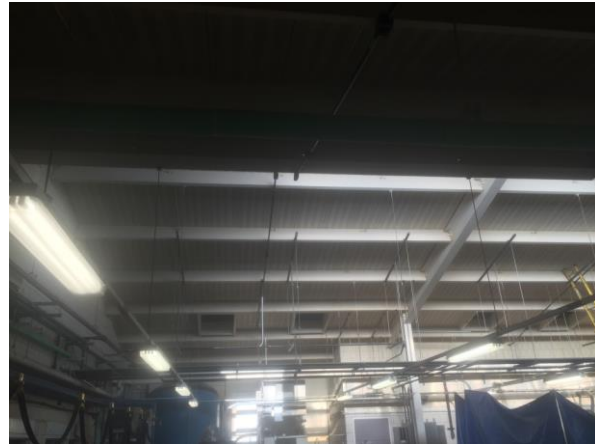

Fire alarm conduit installation along ceiling of Filter Room 1 & 2.



Installation of new fire alarm conduit runs in Filter Room 1 & 2.



Completed epoxy coating of Filter No. 2 effluent channel walls.

II. Construction / Public Relation Issues:

- The contractor was reminded to maintain a safe work environment.

III. Erosion and Sedimentation Control:

- The contractor maintained the silt sock placed at the bottom of the front slope.
- Erosion control will be monitored and maintained throughout the project.

IV. Upcoming Work for Next Week:

- Filter No. 2 – Sand Installation
- Filter No. 2 – Cleanup
- Filter No. 1/2 – Fire alarm electrical

V. Notes:

- The next progress meeting is scheduled for Wednesday, May 4, 2016.

Ted Angelakis
AECOM Resident Representative
