



# TEWKSBURY WTF IMPROVEMENTS PROJECT

Weekly Progress Report for Week Ending: July 8, 2016

Design Engineer: AECOM  
General Contractor: Kinsmen Corporation

## I. Work Performed Last Week:


- Crews continued to set forms around the new Flow Equalization Basin.
- Crews started the excavation for the foundation of the new Laboratory/Break Room Addition.
- The contractor started the demolition of the existing laboratory and administrative areas.
- The crews continued work on the HVAC demolition in the Chemical Room areas.
- The crews continued to demolish existing concrete equipment pads.
- The electrical subcontractor continued to install new fire alarm electrical conduits in different sections of the plant.
- The crews started cleaning the painted areas in the chemical areas.



*Excavation for new Laboratory/Break Room Addition.*



*Formwork for roof slab of new Flow Equalization Basin.*

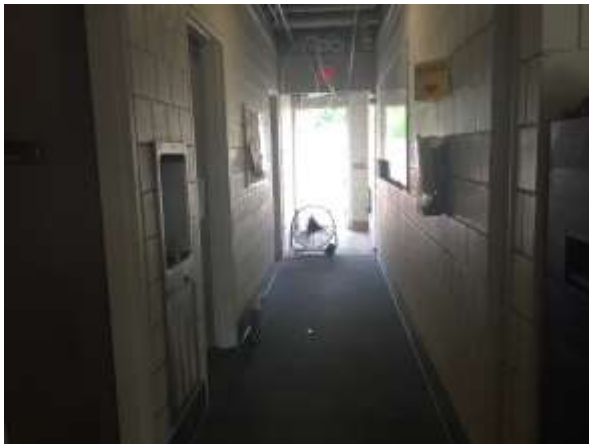

*Removal of back entrance door.*



*Demolition of vestibule area at front entrance door.*

## **II. Construction / Public Relation Issues:**

- The contractor was reminded to maintain a safe work environment.

## **III. Erosion and Sedimentation Control:**

- The contractor maintained the silt sock placed at the bottom of the front slope.
- Erosion control will be monitored and maintained throughout the project.
- Additional temporary fence and erosion control were maintained along the back side of the slope near the new Flow Equalization Basin.

## **IV. Upcoming Work for Next Week:**

- Equalization Basin – Roof slab rebar, form installation and concrete pour.
- Continued demolition of the existing systems; plumbing, HVAC.
- New conduit installation in the plant chemical and diatomaceous earth areas.
- Continued demolition of the existing laboratory.
- Paint prep in the Chemical Room areas.

## **V. Notes:**

- The next progress meeting is scheduled for Thursday, July 14, 2016.

*Ted Angelakis*  

---

**AECOM Resident Representative**
